



# MONTHLY REPORT

UNIVERSITY OF RICHMOND  
WELL-BEING CENTER & QUEALLY  
ATHLETICS CENTER

NOVEMBER 2019

---

**Barton Malow Company**

*Authored by: Eric Follo*

---

# MAN HOURS AND SAFETY

MAN HOURS	RECORDABLE INCIDENTS
16,693	0

## TOP ACTIVITIES FOR NOVEMBER

- Continued exterior wall framing/sheathing
- Exterior air barrier installation
- Completed court roof installation
- Attic framing and decking
- Continued interior MEP rough-ins
- Began Millhiser 4<sup>th</sup> floor duct installation
- Began interior wall framing
- Prep for remaining concrete slab pours
- Completed equipment screen wall steel erection
- Completed east foundation waterproofing
- Backfill of east foundation

## CONTRACTORS ON SITE

CONTRACTOR	TRADE
ETEC	Mechanical & Plumbing
Commercial	Electrical
CT Purcell	Utilities & Earthwork
Piedmont	Concrete
Masonomics	Masonry
Liphart	Steel
Atlantic Contractors	Fire Suppression
Bay	Waterproofing



---



AERIAL DRONE PHOTO






# PROGRESS PHOTOS

## Exterior Framing/Sheathing and Air Barrier

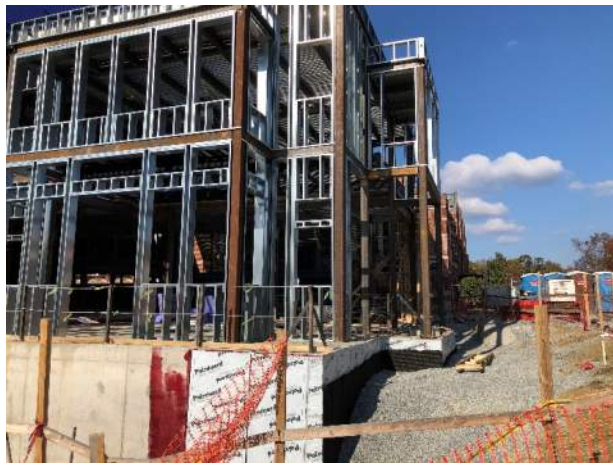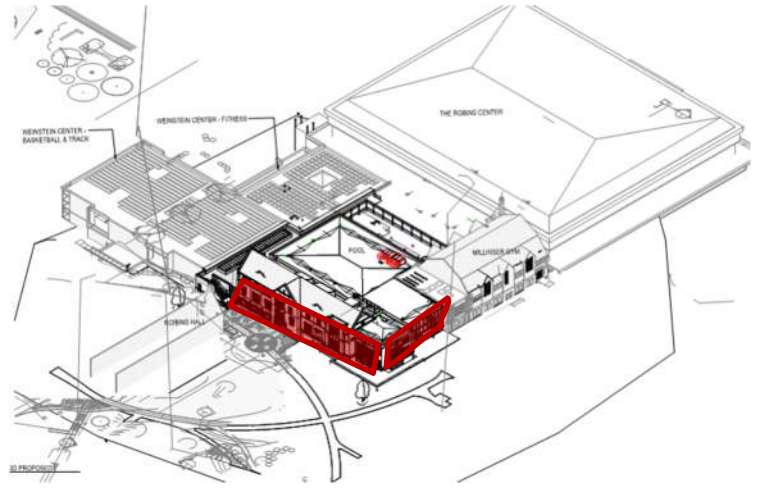




# Interior MEP Rough-in

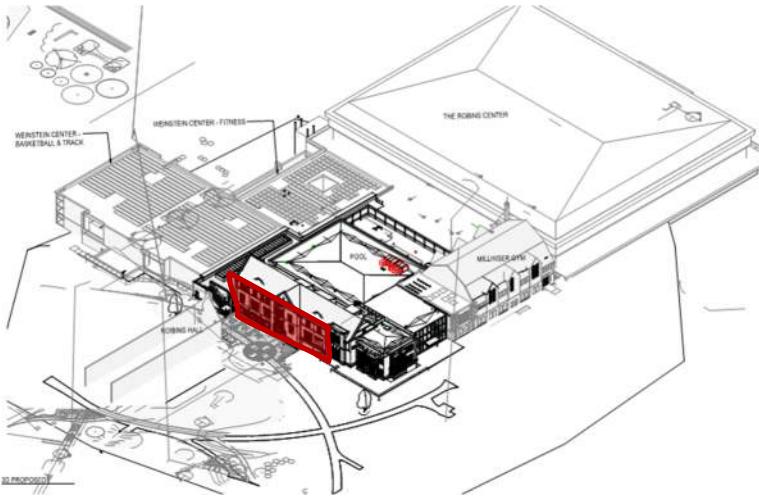




# Attic Framing and Decking

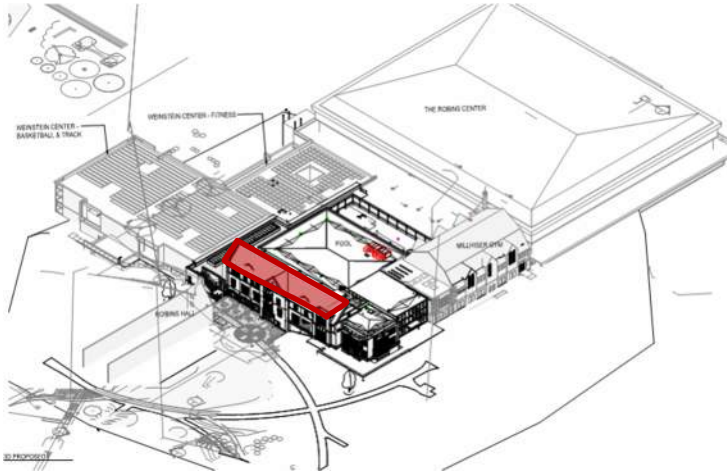





## Interior Wall Framing

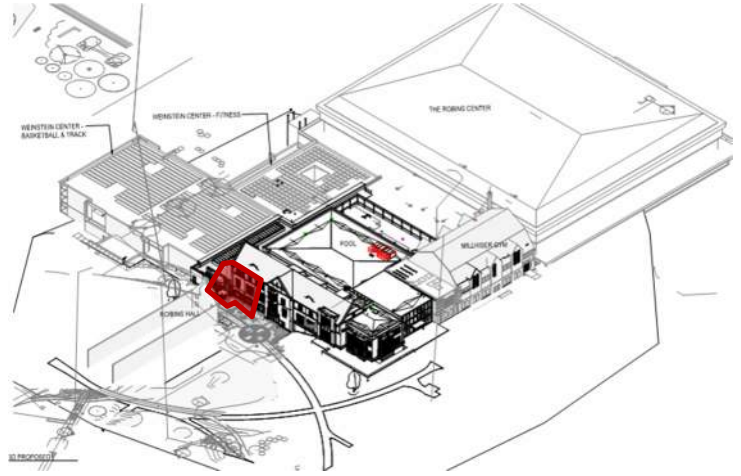

## Millhiser Duct Installation

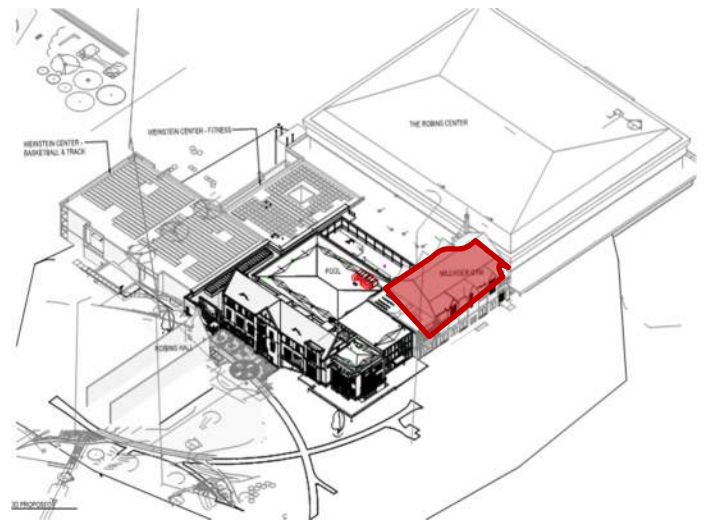


## Court Roofing

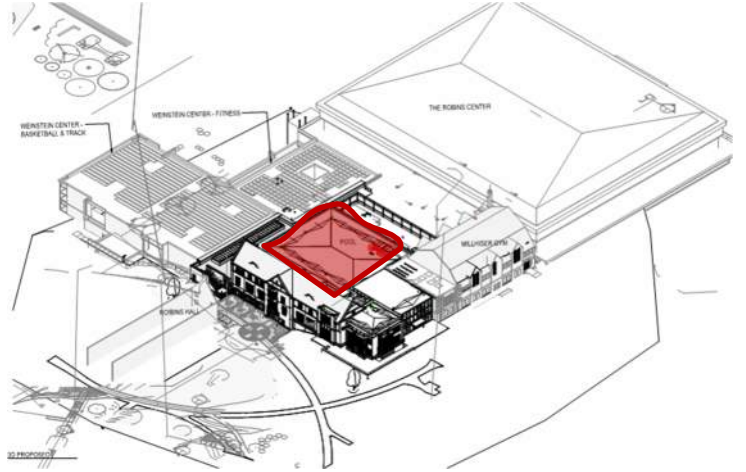



## Team/Locker Room Slab Prep

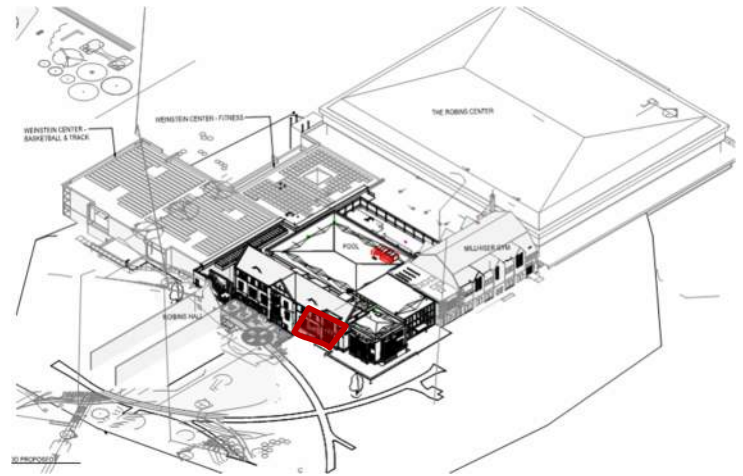


### TOP ACTIVITIES FOR DECEMBER

- Complete remaining concrete slab pours
  - Locker/team rooms
  - Spider Hall bridge
  - Café BOH
- Continue air barrier installation
- Install slate roof underlayment
- Interior wall framing
- Continue flat roof installation
- Continue with interior mechanical, plumbing and electrical overhead rough-ins
- Masonry installation at terrace
- South foundation waterproofing and backfill
- Site utility installation
- Millhiser – 3<sup>rd</sup> and 4<sup>th</sup> floor duct installation
- Weinstein opening demolition

## UPDATED SCHEDULE

**\*SEE ATTACHED SCHEULE\***

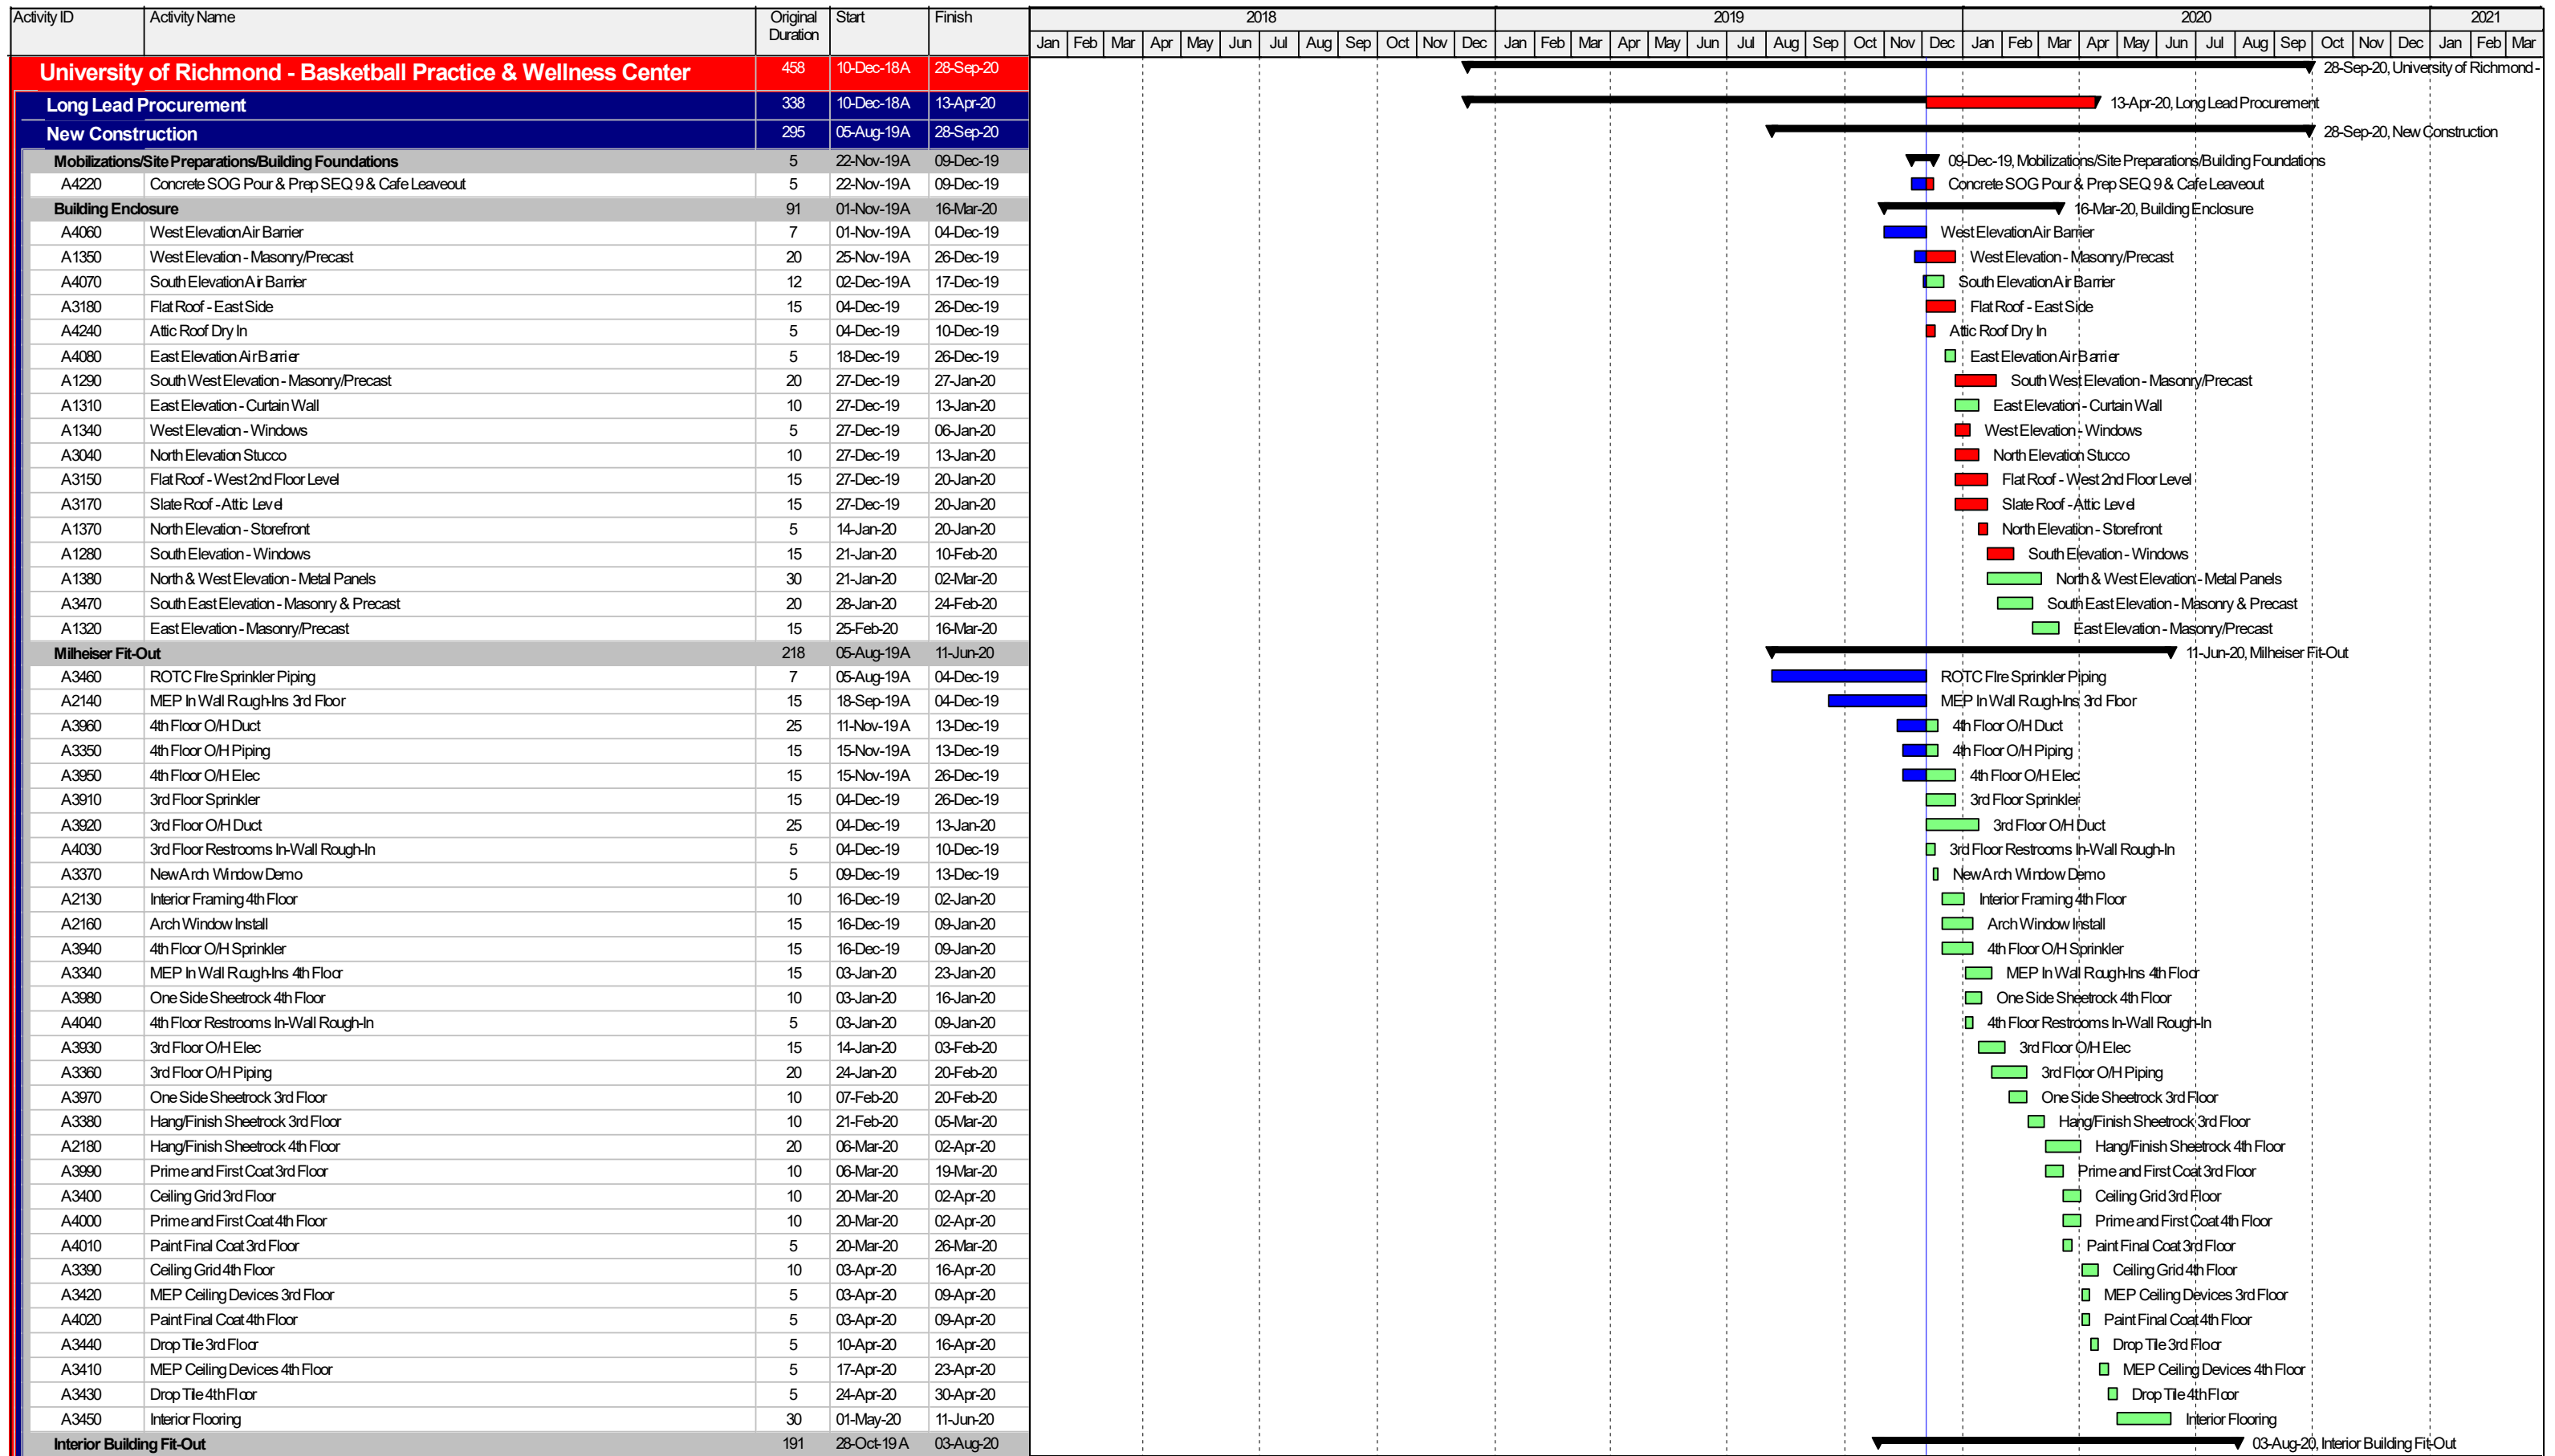

Project ID: 180333  
 Print Date: 04-Dec-19 17:38  
 Data Date: 04-Dec-19  
 Project Start: 01-Mar-18  
 Project Finish: 28-Sep-20  
 Page: 1 of 3



**University of Richmond -  
Basketball Practice Wellness  
Center**







Activity ID	Activity Name	Original Duration	Start	Finish	2018												2019												2020												2021																															
					Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar																													
A2240	Project Complete	0		28-Sep-20																																																																				

◆ Project Complete



**University of Richmond -  
Basketball Practice Wellness  
Center**

